

Parkside Huntingdale Stage Update – Stage 2

25/09/2025

We are currently holding to the revised timeline, with titles anticipated in June 2026. The external sewer works remain the critical path, and progress is being closely monitored through our regular site meetings and consultant updates.

Regular site meetings and inspections will continue, and we will keep you updated as milestones are reached.

KEY MILESTONES

Construction Start Date – August 2025

Practical Completion Date (PC) - May 2026

Titles Anticipated - June 2026

CLEARANCES

Council - Pending.

Department of Education - Pending.

Water Corporation - Pending.

Western Power - Pending.

Department of Planning, Lands and Heritage - Pending all other clearances.

Landgate - Application for Titles to be lodged.

CIVIL CONSTRUCTION

Earthworks - 0%

Sewer - 0%

Stormwater - 0%

Water - 0%

Power Internal - 0%

Power External - 0%

Communications - 0%

Gas - 0%

Roads

Subgrade - 0%

Limestone - 0%


Asphalt 40 mm - 0%

Asphalt 30mm (final layer) - 0%

Kerbs - 0%

Footpaths - 0%

All dates provided are estimates and subject to change.

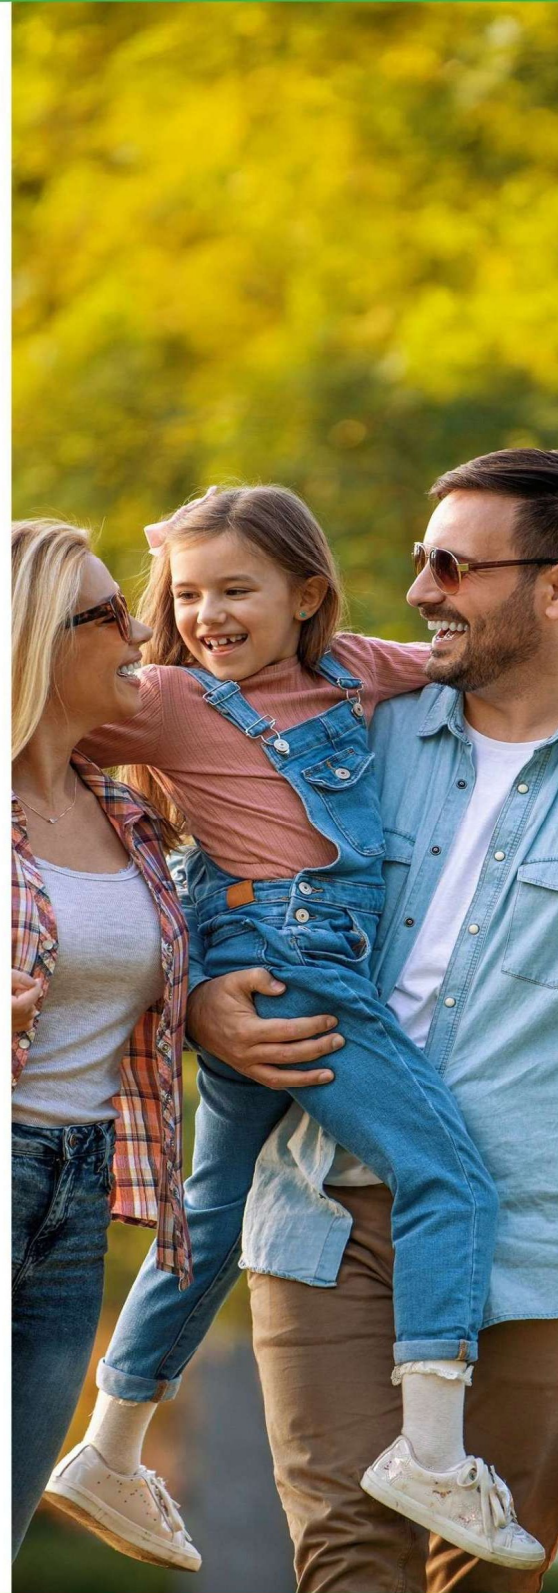

Whilst we always aim to provide accurate completion dates, we apologise for the delay and appreciate your understanding during this challenging build period. We're working hard to keep everyone informed and truly value your continued patience.

We endeavour to provide accurate dates of completion and titles, these dates can change depending on site conditions, weather delays, the speed at which the Statutory Authorities process our clearances, and Landgate issues Certificate of Titles.

