

Parkside Huntingdale Stage Update – Stage 3

18/08/2026

The information below will provide you with the latest information following our fortnightly site inspections, and updates from our consultants.

Whilst we will always endeavour to provide accurate dates of completion and titles, these dates can change depending on site conditions, weather delays, the speed at which the Statutory Authorities process our clearances and Landgate issues Certificate of Titles.

We are pleased to advise that Stage 3 civil construction has commenced as expected. The civil contractors are currently focused on bulk earthworks, including clearing across the stage. Over the next fortnight, earthworks will continue as the crew progresses with the broader site preparation works. The contractor is meeting all Council requirements and is actively managing the works around the weather conditions being experienced.

KEY MILESTONES

Construction Start Date – July 2026

Practical Completion Date (PC) – February 2027

Titles Anticipated - March 2027

CLEARANCES

Council - Pending.

Department of Education - Pending.

Water Corporation - Pending.

Western Power - Pending.

Department of Planning, Lands and Heritage - Pending all other clearances.

Landgate - Application for Titles to be lodged shortly.

CIVIL CONSTRUCTION

Earthworks - 0%

Sewer - 0%

Stormwater - 0%

Water - 0%

Power Internal - 0%

Power External - 0%

Communications - 0%

Gas - 0%

Roads

Subgrade - 0%

Limestone - 0%


Asphalt 40 mm - 0%

Asphalt 30mm (final layer) - 0%


Kerbs - 0%

Footpaths - 0%

All dates provided are estimates and subject to change.

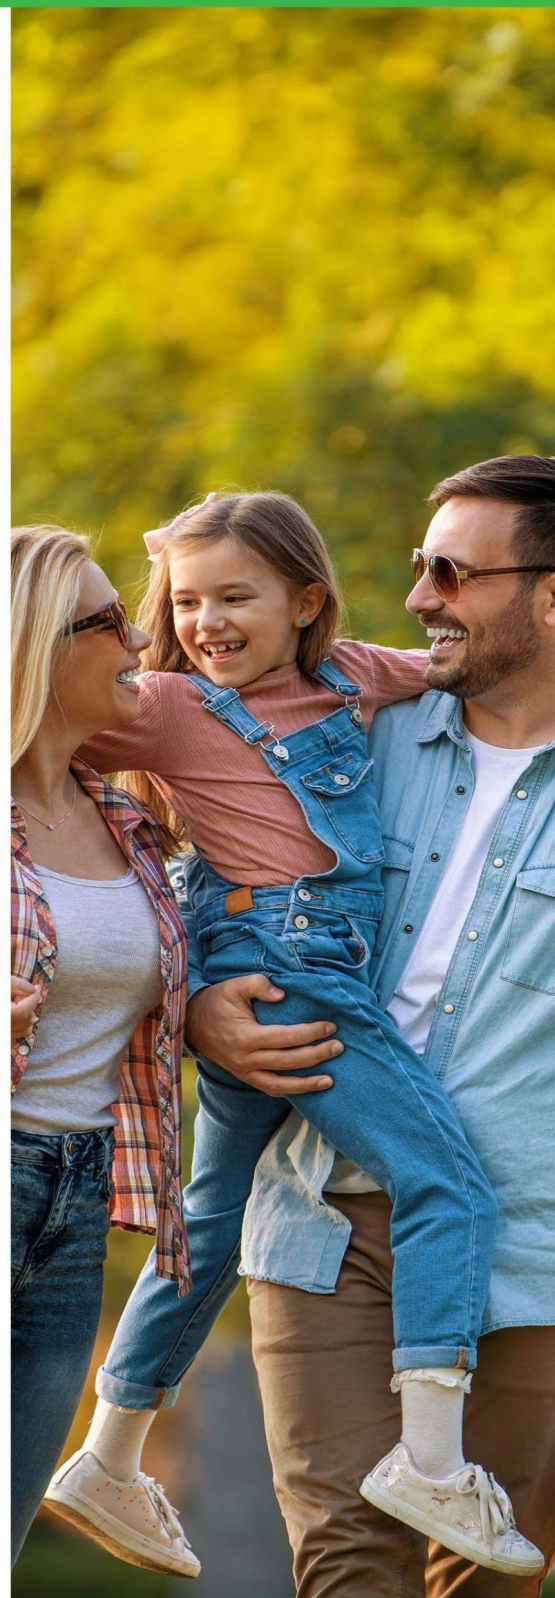

Whilst we will always endeavour to provide accurate dates of completion and titles, these dates can change depending on site conditions, weather delays, the speed at which the Statutory Authorities process our clearances, and Landgate issues Certificate of Titles.

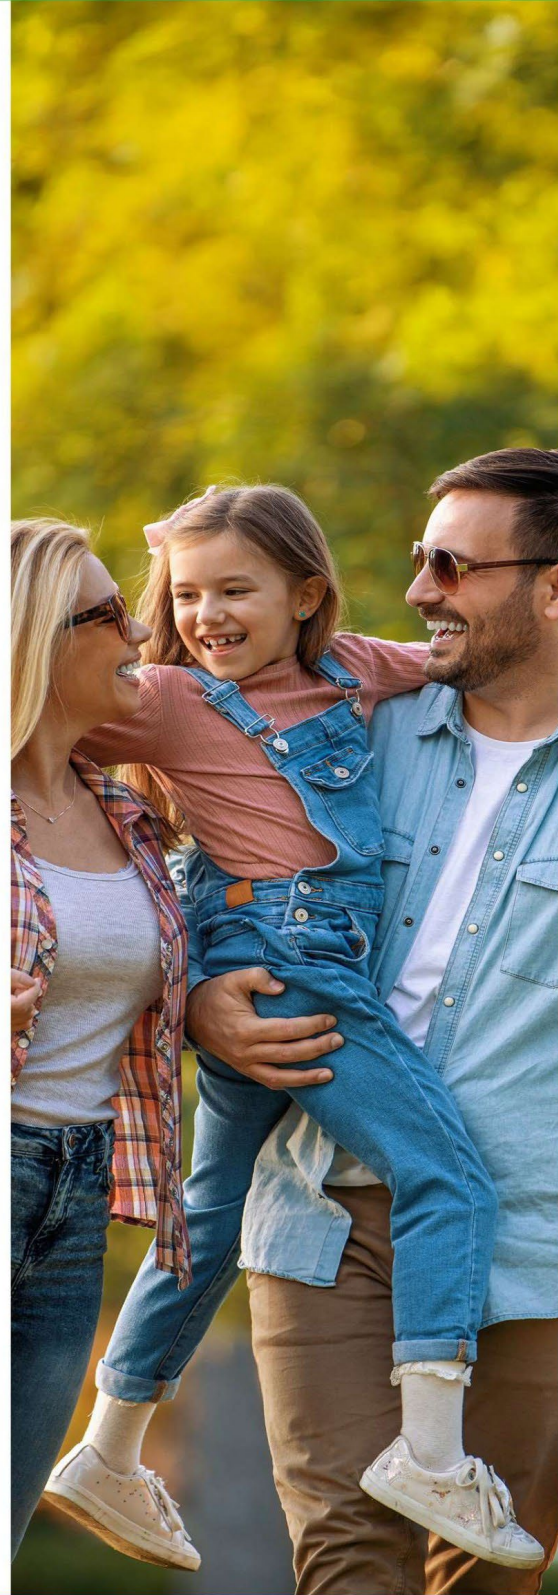

Call Robert Wnek on 0419 335 412 or visit
parksideprivateestate.com.au

PROGRESS
DEVELOPMENTS

PARKSIDE
HUNTINGDALE
