

Parkside Huntingdale Stage Update – Stage 3

15/10/2026

Stage 3 civil construction is ongoing and remains on track with the current civil construction program. The civil team is currently progressing with a heavy focus on drainage and sewer construction. Common services are forecast to start over the next fortnight.

We appreciate your patience and understanding while earthworks and civil construction are underway. We will continue to provide updates as works progress and further milestones are reached.

KEY MILESTONES

Construction Start Date – July 2026

Practical Completion Date (PC) – February 2027

Titles Anticipated - March 2027

CLEARANCES

Council - Pending.

Department of Education - Pending.

Water Corporation - Pending.

Western Power - Pending.

Department of Planning, Lands and Heritage - Pending all other clearances.

Landgate - Application for Titles to be lodged shortly.

CIVIL CONSTRUCTION

Earthworks - 60%

Sewer - 50%

Stormwater - 30%

Water - 0%

Power Internal - 0%

Power External - 0%

Communications - 0%

Gas - 0%

Roads

Subgrade - 0%

Limestone - 0%


Asphalt 40 mm - 0%

Asphalt 30mm (final layer) - 0%

Kerbs - 0%


Footpaths - 0%

All dates provided are estimates and subject to change.

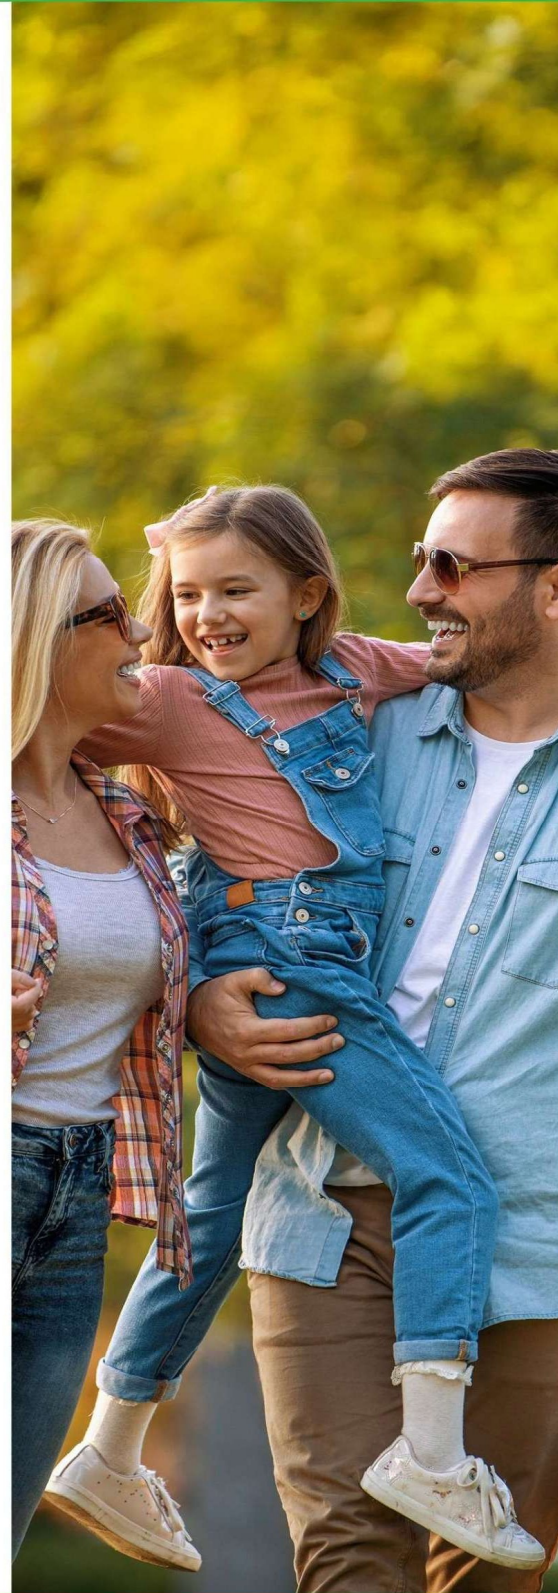

We endeavour to provide accurate dates of completion and titles. These dates can change depending on site conditions, weather delays, Statutory Authority processing times and Landgate title issuance.

We thank you for your patience and understanding.

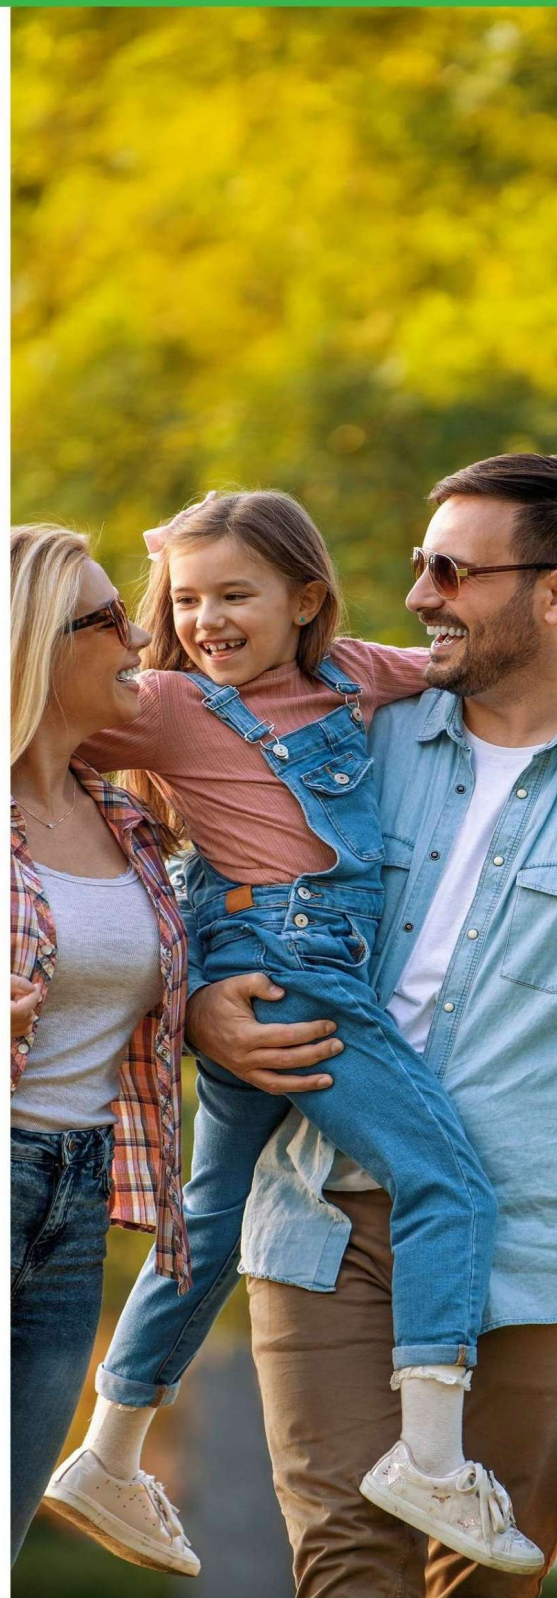

Call Robert Wnek on 0419 335 412 or visit
parksideprivateestate.com.au

PROGRESS
DEVELOPMENTS

PARKSIDE
HUNTINGDALE
